

Church and John Street Revitalisation

Project Update – July/August 2022

As part of the ongoing revitalisation of its City Centre, the City of Salisbury is delivering the renewal of Church and John Streets, which continues to create a sense of place that reflects Salisbury's heart and identity.

John Street

Major works are continuing along John Street, moving east from Gawler Street towards Ann Street. Works include:

- Construction of new concrete kerbing and planter beds
- Installation of irrigation for planter beds and new trees
- Levelling of service pits and surrounding pavement

Up to 15 car parks along John Street are temporarily closed. Closures will last approximately two weeks in each section, as the works move east along John Street. Works are being staged to minimise these impacts where possible. Localised short-term closures will occur occasionally throughout the Project to allow for specific tasks.

Conduit installation works are also being undertaken on John Street to facilitate the new Smart City and its lighting. Where possible, to minimise footpath closures, directional drilling is being utilised in addition to open trenching.

Sexton Carpark


Drainage and pavement works in the Sexton Carpark have now moved to the eastern end of the carpark. As these works continue, some sections of the carpark will remain closed. Various detours remain in place for vehicles and pedestrians.

Church Street

Drainage and pavement works are being undertaken along the northern end of Church Street, between James Street and John Street. Temporary Lighting will be installed over the coming weeks as an interim condition.

Trenching and boring works to facilitate LED lighting are also being undertaken.

Timeline

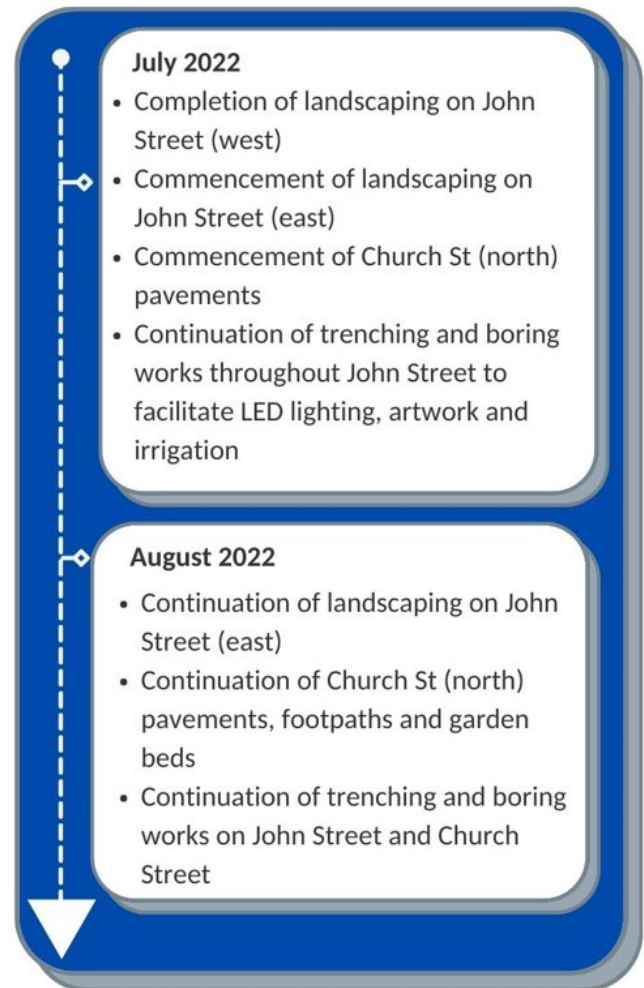

The above timeframes are indicative and subject to change.

The project is expected to be completed in late 2022, weather permitting.

Works are being undertaken from 7am to 5pm, Monday to Friday. Some weekend work may be required.

Questions and feedback

We continue to work with businesses, building owners and the community during construction to manage specific requirements.

Church and John Street Revitalisation

Project Update – July/August 2022



To make an enquiry or to register to receive email updates as the project progresses, please contact us by:

Emailing: stratdev@salisbury.sa.gov.au or

Calling: 1300 539 552

Updates will also be provided on the City of Salisbury webpage:

www.salisbury.sa.gov.au/churchandjohnst

Thank you for your patience during construction.
