

# Church and John Streets Revitalisation

## Project Update – August 2022

As part of the ongoing upgrade of its City Centre, the City of Salisbury is delivering the revitalisation of Church and John Streets, which continues to create a sense of place that reflects Salisbury's heart and identity.


The precinct has experienced a great amount of transformation recently, and we are proud to share the progress of this important project with you. Thank you for your ongoing patience and support.



### New landscaping

The installation of new garden beds along Church and John Streets is nearing completion. The mixture of native and non-native plants will enrich the character of the street and once established will provide shade for visitors.

New trees and shrubs are expected to be planted in October 2022, delivering a greener and more attractive streetscape complementing the new spaces created for traders to use for outdoor dining.

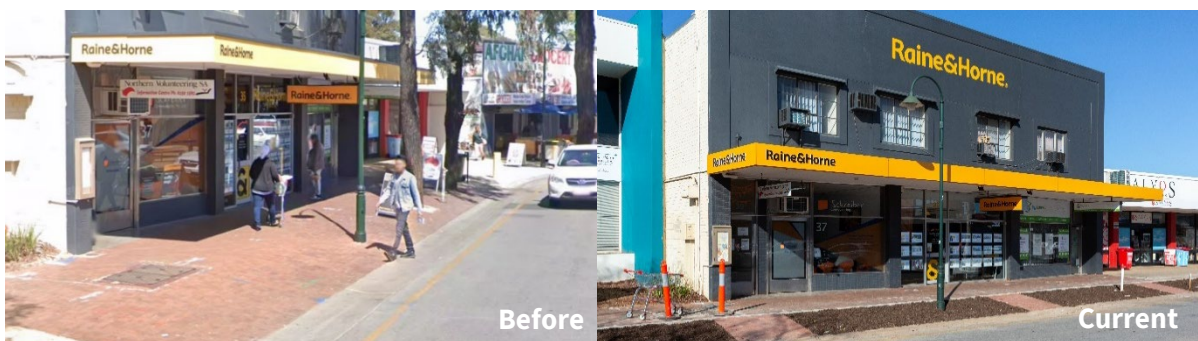


*John Street before and current landscaping treatments (with new plantings to occur in October 2022).*



# Church and John Streets Revitalisation

## Project Update – August 2022

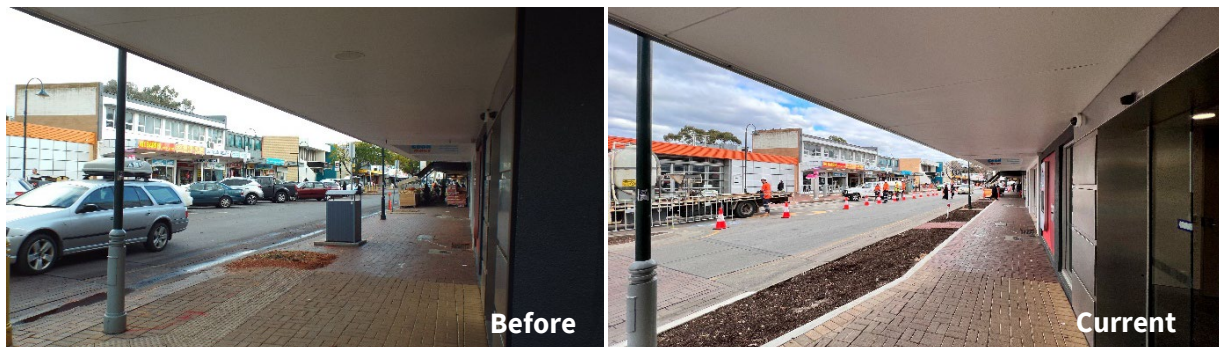

*Landscaping treatments on John Street*

### Improved pedestrian connections

Throughout the precinct there have been several accessibility improvements for pedestrians. New kerbing, footpaths and access ramps have been installed along Church Street. This provides better connection between the Salisbury Civic Plaza and local businesses.


To create a fresh and consistent look and feel throughout the precinct, some existing paving is being cleaned and renewed.

Areas where paving has sunk or moved due to ground conditions or tree roots are being repaired. Tactile pavers are being removed except for key pedestrian crossing points. The removal of bollards, street furniture, old trees and tower signage (at the western end of John Street) will open up the precinct and make it easier and safer to travel along Church and John Streets. These works are scheduled for completion in October 2022.

Connection to Hoyts Cinema, via the Sexton Lane and the Sexton Carpark, will be improved through new LED lighting and upgraded pedestrian pathways. Stormwater works in the Sexton Carpark have improved drainage in an area that has previously experienced temporary flooding during rain events, with these carparks now open.

Adelaide Metro Bus stop 49/B from outside the Salisbury Bakery has been relocated to Wiltshire Street. Bus stop 49/A at the Salisbury Civic Plaza will be relocated to outside the Salisbury Bakery in September following completion of footpath reconstruction in this location.

The Department for Infrastructure and Transport will provide signage communicating which buses will stop at each location in both temporary and ongoing arrangements.

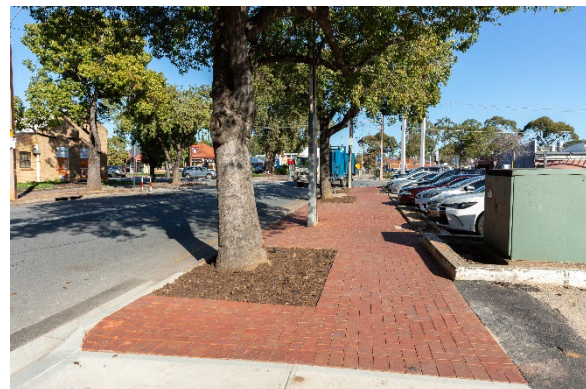

*Landscaping and new footpaths on Wiltshire Street*

# Church and John Streets Revitalisation

## Project Update – August 2022



*New footpaths and current landscaping treatments on Wiltshire Street (new plantings to occur in October 2022)*

Works to install new bench seats, drink fountains, lighting and new accessible public toilets are expected to be undertaken by January 2023. These new modern amenities will help to support local traders and provide cleaner and safer facilities for shoppers and visitors.

### More accessible carparking

Sexton Carpark has been reconfigured to accommodate the new public toilets and to improve pedestrian access and carparking. Several new accessible parking bays will also be created in the carpark. Drainage, footpath and pavement work in the carpark are now almost complete.

Whilst there have been some temporary restrictions to car parking along John Street and Church Street during the works, work zones are being established to minimise the number of parks that are impacted at any one time.

### New Lighting, CCTV and Wi-Fi

Trenching and boring works are being undertaken to accommodate the installation of new LED lighting, CCTV, Wi-Fi, irrigation, artwork and public toilets. These in-ground works are expected to be completed by mid-September. The City's new smart infrastructure is anticipated to be commissioned by January 2023.

The new light poles will improve safety and create a modern look throughout the precinct, complimenting the new trees, landscaping and spaces created for outdoor dining.



*Trenching works being undertaken to install underground infrastructure to accommodate new LED lighting, CCTV, Wi-Fi and irrigation*



# Church and John Streets Revitalisation

## Project Update – August 2022



### Service Provider Works

Over the coming months, service providers including power, gas and water will undertake localised works across the precinct to improve the condition of their assets. Individual service providers will provide advance notification to advise of their various works and programming.

### Timeline

These timeframes are indicative and subject to change.

**The project is anticipated to be complete in January 2023, with the majority of activities complete by early November 2022.**

Works are being undertaken from 7am to 5pm, Monday to Friday. Some weekend work may be required.

### Questions and feedback

We continue to work with businesses, building owners and the community during construction to support specific requirements.

To make an enquiry or to register to receive email updates as the project progresses, please contact us:

Email: [stratdev@salisbury.sa.gov.au](mailto:stratdev@salisbury.sa.gov.au) or

Call: 1300 539 552

Updates will also be provided on the City of Salisbury webpage:

[www.salisbury.sa.gov.au/churchandjohnst](http://www.salisbury.sa.gov.au/churchandjohnst)

**Thank you for your patience during construction.**

